


IND713/MEC713 – FALL 2023
Resource Allocation Lab
General Instructions


1. Read the instructions in the handout. You will complete the activities of this lab individually.
2. Build one Microsoft Project file and one Microsoft Word file based on the instructions.
3. Submit the Microsoft Project file and the Microsoft Word file in D2L. The name of the section in D2L is “Practicum 5” or “Lab 5”.
4. Submission must be made before the end of your lab in D2L.
5. Your submission will be graded out of 15.

For this project, you need to **open a Microsoft Project file**. You may type **Project** (in *Type here to search*) in the desktops of the computers in the labs to find it. Then, **save** the files as **Project, your first and last names**. Example: Project, John Li. You may save it on the desktop. So you can find and upload it in D2L after completing the file. You also need to create a Microsoft Word file, and upload it in D2L (save it as **Questions, your first and last names**). Example: Questions, John Li.

- You can find several options about “Resource” in Microsoft Project.



- You can add a task to MSP. Then, right click on the task, then, select “Assign Resources”.

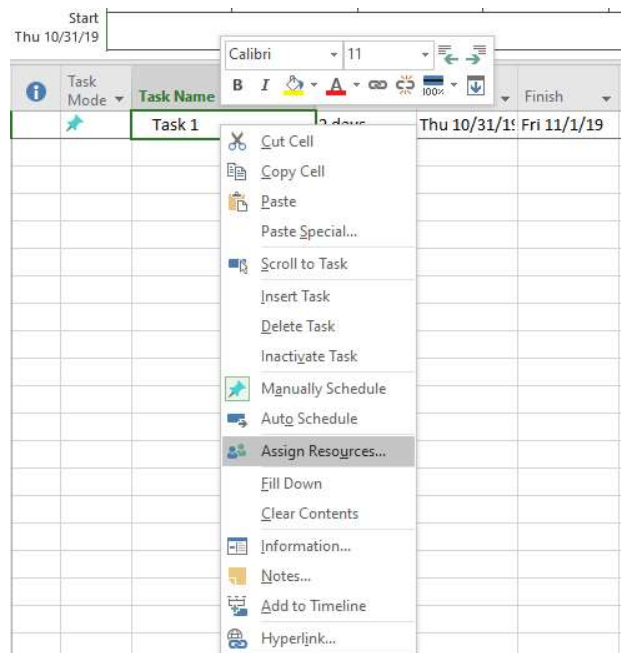

John's SHED Project

John wants to create a shed for the storage of his lawn tools, equipment and other small items he wants to get out of the garage. The shed will be built from a kit that can be ordered from Home Depot.

The wall needs to be 8ft tall; floor space needs to be 120 sq. Ft. 2' x3' windows on each side. It is required to have double doors on the front side to create a 7' x 8' opening, lockable. The roof will be shingled to match the house, cedar siding stained to match the house. Leave rafters open for additional storage, concrete slab floor.

Location: SW corner of the backyard.

Estimated duration – 4 weeks.

- Open a Microsoft Project file.
- Save the file as **Project, your first and last names**.

Part 1: Create a Project Schedule

- a) Enter the task name, task duration and predecessors in Table 1 into Microsoft project, to create a project schedule and Gantt Chart.


Table 1 Schedule

Task ID	Task Name	Duration	Predecessors
1	Order Kit and schedule delivery	1 day	
2	Preparation	0 days	1
3	Site preparation - Clear and level the landscape	2 days	
4	Pour the foundation	1 day	3
5	Receive delivery of kit	1 day	4
6	Delivery Milestone	0 days	5
7	Assembly	2 days	6
8	Assemble Kit	2 days	6
9	Stain the Shed	1 day	6
10	Plant landscaping/flowers	1 day	6
11	Fill shed	1 day	7,8,9,10

Note: Preparation and Assembly are summary tasks.

Part 2: Create a Resource Sheet

- a) Create a resource sheet with the following data given in Table 2.
b) Assign the resource type and resource rate.



Hint: You can click

Table 2 Resource Names

Resource Name	Resource Type	Resource rate (Std. Rate)
Andy Holmes	Work	\$25.00/hr
Betty Scholes	Work	\$10.00/hr
Frank Homes	Work	\$10.00/hr
Home Owner (John Doe)	Work	\$0.00/hr
Shed Kit	Material	\$1,250.00

Part 3. Assign resources


- Assign the resources in Table 3 to the respective tasks.
- Select the view tab, on the split view group. *If task form isn't selected from the drop-down menu, select "task form".*
- When assigning project resources, make sure that the **task type** is "**Fixed Duration.**" (you can find it by double clicking on the Task Name, then in "Task Information" box).

Table 3: Assigned Resources


Task ID	Duration Days	Assigned Resources	
		Resource Name	Work
1	Order Kit and schedule delivery	Home Owner (John Doe)	2h
		Shed Kit	1
2	Preparation		
3	Site preparation - Clear and level the landscape	Betty Scholes	8h
		Frank Holmes	8h
		Home Owner (John Doe)	8h
4	Pour the foundatuon	Home Owner (John Doe)	5h
		Andy Holmes	5h
5	Receive delivery of kit	Home Owner (John Doe)	2h
6	Delivery Milestone		
7	Assembly		
8	Assemble Kit	Andy Holmes,	10h
		Home Owner (John Doe)	10h
9	Stain the Shed	Andy Holmes,	2h
		Home Owner (John Doe)	2h
10	Plant landscaping/flowers	Betty Scholes	4h
11	Fill shed	Frank Homes	5h
		Home Owner (John Doe)	5h

Part 4: Microsoft Project Report

- a) Set project baseline: Go the Project tab, select set baseline, select set baseline from the drop-down menu, select *for entire project*, click ok.



- b) In the add new column drop-down menu, select *% complete*.




- c) Enter the progress % in Table 4 into the project (**Note:** a check mark will appear in the indicator column on the left side of the screen showing the task is complete).

Table 4. The progress %

Task Name	Progress %	Actual Cost (\$)
Order Kit and schedule delivery	100	1400
Site preparation - Clear and level the landscape	100	180
Pour the foundation	100	130
Receive delivery of kit	100	0
Assemble Kit	100	300
Stain the Shed		
Plant landscaping/flowers		
Fill shed		

- d) In the add new column drop-down menu, select *Actual Cost*.
e) Enter the Actual cost in Table 4 into Project.
f) Select **Report tab**, select **Dashboards**, from the drop-down menu, select **cost overview**.



Create a Microsoft Word file. Answer the following questions in the file, and save it.

1. What is the total cost of the project?
2. What are the cost variances?
3. What is the remaining cost of the project?
4. How much of the project was completed?

Upload both your **Microsoft Word file** and **MSP file** in D2L.
